

SPB Number: 2022.0304

EXTERIOR UPDATE

[X] All Travel Center Stores

THE CLIPS BELOW ARE TAKEN FROM THE LH PROTOTYPE

Issued: 10/20/2022

STANDARD PLAN BULLETIN NOTICE
RaceTrac Engineering and Construction Division

1. **PARAPET UPDATE:** Raised all the parapet heights to conceal the RTUs.

- Sheets: A126, A300, A410, A411, A420, A421, A422, A423, A430 & S201
- Attachments: A300

T.O. TOWER	24' - 5 1/4"	
T.O. CORNER TOWER	23' - 2 1/8"	
T.O. PARAPET (MED)	21' - 6 3/8"	
T.O. PARAPET (LOW)	20' - 3 3/4"	

2. **BRICK UPDATE:** Updated brick to be queen brick with 1/3 running bond pattern. Updated soldier course design to align with queen brick coursing.

- Sheets: A010-1, A010-2, A010-3, A010-4, A010-5, A011-3, A011-4, A012, A013-2, A126, A201, A300, A410, A411, A420, A421, A422, A423, A430, A431, A601, A701, C101, S200 & S433
- Attachments: A300

BRICK		
BR-1	US BRICK	LAREDO (QUEEN 1/3 BOND)
BR-2	US BRICK	MOUNT RUSHMORE (QUEEN 1/3 BOND)


3. **DOWNSPOUT UPDATE:** Updated the size of the downspouts for the canopies to be 2"x2".

- Sheets: A100, A200 & A300
- Attachments: A100

7	2"x2" DOWNSPOUT, TIE TO UNDERGROUND STORM, SEE CIVIL FOR CONTINUATION; REF DETAIL 3/A110
---	--

4. **SUPPORT RACK:** Updated the support rack dimensions for condensers and make-up air unit.

- Sheet: S200
- Attachments: S200

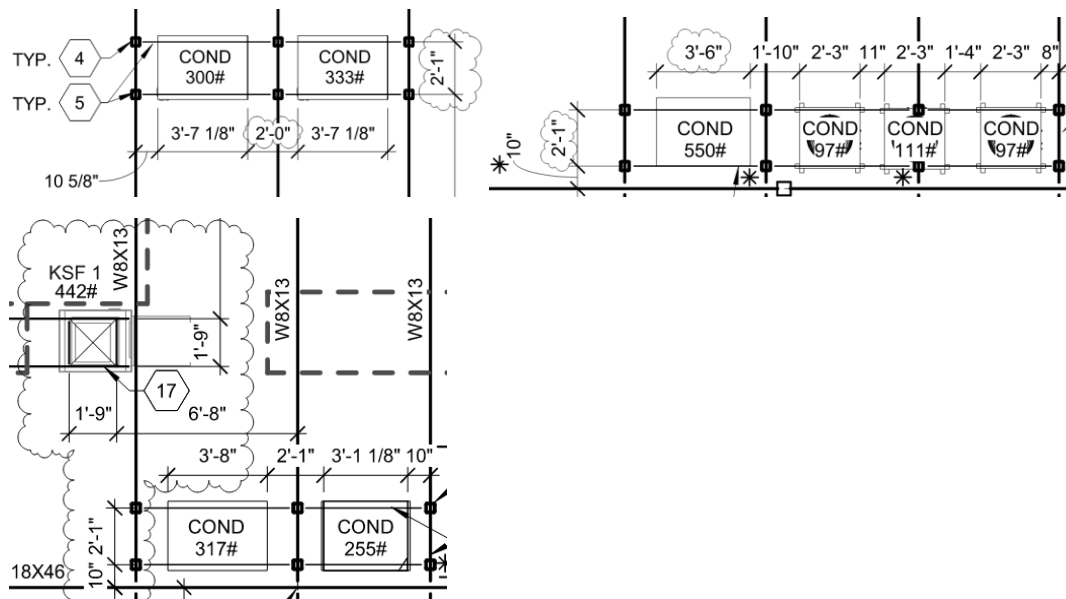

5. **ACCESS DOOR:** Added access door at the towers.

- Sheets: A201, A410, A423 & A700
- Attachments: A201

